

KENDRIYA VIDYALAYA SANGATHAN (WORKS DIVISION)

**STATUS OF ON GOING
CONSTRUCTION WORK OF SCHOOL
BUILDING PROJECTS**

AS ON

01.11.2018





Status of Ongoing Construction work of School Building Projects as on 01.11.2018(State Wise)

Sl. No.	Name of Kendriya Vidyalaya	AA & ES (Rs. in lakh)	Date of Sanction	Construction Agency	Date of Start	Physical Progress upto date	Stipulated date of completion	Amount released till date (Rs. in lakh)	Remark
1	2	3	4	5	6	7	8	9	11

(A) SCHOOL BUILDING UNDER CONSTRUCTION

Andhra Pradesh

1	Tenali (A-I type+09 SQ+BW)	1600.94	05.10.2015	HSCCL	17.02.16	84%	16.08.17	1420.00	180.94	Work in Progress TDC- 30.06.2018
---	-------------------------------	---------	------------	-------	----------	-----	----------	---------	--------	--

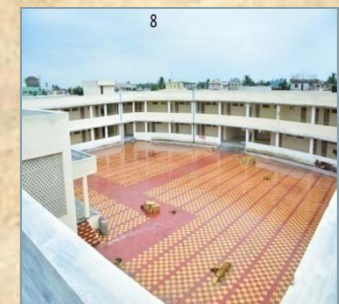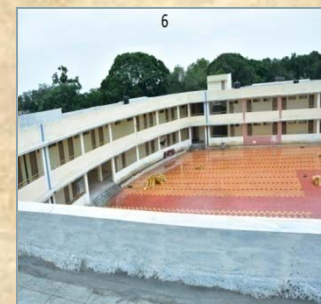

Arunachal Pradesh										
2	Miao (A-I type +09 SQ+BW)	2383.70	13.01.2015	AP PWD	01.08.15	45%	March,2019	1700.00	683.70	Slow Progress due to N.E. Region problem.



3	Tuting (A-I type+09 SQ+BW)	2431.81	12.10.2015	AP PWD	10.01.16	45%	March,2019	1320.00	1111.81	Slow Progress due to N.E. Region problem
---	----------------------------------	---------	------------	--------	----------	-----	------------	---------	---------	---



Assam

4	Rangiya (B-Type+SB + B/w)	2264.95	01.09.2016 03.05.2017	AP PWD	16.01.17.	80%	31.08.18	2020.00	244.95	Work in progress.
---	------------------------------	---------	--------------------------	--------	-----------	-----	----------	---------	--------	-------------------



5.	Haflong (A-Itype+09 SQ)	1751.23	15.12.2010	CPWD	13.08.13	96%	03.02.15	1750.00	1.23	Initial delay due to land dispute. TDC-31.12.18
----	----------------------------	---------	------------	------	----------	-----	----------	---------	------	--



6.	Tamulpur (Atype+09 SQ+BW)	2196.62	12.09.2014 24.04.2015	CPWD	07.10.15	99%	06.04.17	2195.00	1.62	T.D.C-30.06.18 Slow progress due to shortage of fund..TDC- 31.08.18
----	------------------------------	---------	--------------------------	------	----------	-----	----------	---------	------	---



7.	Golaghat (A-ltype+11 SQ+BW)	1885.41	08.05.2014	CPWD	27.04.15	98%	26.10.2016	1820.00	65.41	Delay/slow progress due to shortage of fund. TDC-31.12.2018
----	--------------------------------	---------	------------	------	----------	-----	------------	---------	-------	---



BIHAR										
8.	Betia (A-Type+BW)	1301.66	24.06.2014	HSCL	25.07.14	90%	31.01.16	1220.00	81.66	Due to Bandh & Ban on sand. TDC-30.09.18



9.	Aniwan, Jehanabad B-Type+09 Sq+BW	2679.99	04.12.2014	CPWD	19.08.15	85%	18.02.17	2420.00	259.99	Initial delay due to land dispute. TDC-30.09.18
----	--------------------------------------	---------	------------	------	----------	-----	----------	---------	--------	---



Chhatisgarh

10.	No 4 BCPP Korba ('A'-Type+09 SQ+BW)	1586.32	01.09.16	CPWD	24.11.16	87%	23.11.17	1470.00	116.32	TDC-Jan 2019
-----	-------------------------------------	---------	----------	------	----------	-----	----------	---------	--------	--------------



11	Narayanpur ('A'-Type+09 SO+BW)	1694.01	28.02.2017	BBJ&JCC	30.05.2017	44%	August 2018	1120.00	574.01	Go ahead approval given on 31.12.2018
----	--------------------------------	---------	------------	---------	------------	-----	-------------	---------	--------	---------------------------------------



Delhi

12	Sec.-28, Rohini @ ('B' Type)	1800.62	12.08.2014	AP PWD	08.12.17	45%	07.12.19	1120.00	680.62	Delay in approval of Drawings by MCD.
----	-------------------------------	---------	------------	--------	----------	-----	----------	---------	--------	---------------------------------------



Gujarat

13	Dahod ('A' Type + 09 SQ + BW)	1589.37	09.06.2015	CPWD	26.07.16	77%	25.10.17	1100.00	489.37	Initial delay on the part of CPWD.TDC-31.10.2018
----	-------------------------------	---------	------------	------	----------	-----	----------	---------	--------	--



Haryana

14.	No.3 Faridabad ('B' Type SB+9SQ+BW)	2018.22	01.03.2017	DHPD	11.10.17	60%	10.10.19	1420.00	598.22	Work in Progress.
-----	-------------------------------------	---------	------------	------	----------	-----	----------	---------	--------	-------------------



15.	Budayam (Jind) ('B Type + SB+9SQ)	1943.68	26.04.17	CPWD	06.03.18	30%	29.05.19	920.00	1023.68	Work in Progress
-----	-----------------------------------	---------	----------	------	----------	-----	----------	--------	---------	------------------



Jammu & Kashmir

16.	Kargil A-Type	1372.63	01.03.2013	CPWD	15.08.14	85%	14.08.17	1120.00	252.63	Delay due to J&K problem.TDC-31.10.2018
-----	---------------	---------	------------	------	----------	-----	----------	---------	--------	---



17.	Miran Sahib(A' Type+ 09 SQ +BW)	2017.63	09.01.2017	CPWD	17.07.17	40%	16.01.19	1120.00	897.63	Work in Progress.
-----	---------------------------------	---------	------------	------	----------	-----	----------	---------	--------	-------------------



18.	B.S.F. Bandipur ('A-1' Type + 09 SQ + BW)	1606.94	27.07.16	CPWD	30.05.17	23%	29.05.19	620.00	986.94	Work in progress
-----	---	---------	----------	------	----------	-----	----------	--------	--------	------------------



Karnataka

19.	Kodagu ('A-1' - Type+09 SQ+ BW)	1267.79	20.10.2015	CPWD	01.10.16	78%	17.04.18	1220.00	47.79	Work in Progress . TDC-31.12.18
-----	-------------------------------------	---------	------------	------	----------	-----	----------	---------	-------	------------------------------------



20.	Chikodi ('A' - Type+09 SQ+ BW)	1710.97	29.03.2017	CPWD	10.08.2017	22%	10.02.19	620.00	1090.97	Work recently sanctioned.
-----	---------------------------------	---------	------------	------	------------	-----	----------	--------	---------	---------------------------



21.	Koppal A-Type+09 SQ+BW	1713.94	12.09.2014 23.02.2016	HSLC	10.12.2015	60%	12.06.17 TDC-30.09.18	1020.00	693.94	Initial delay on account of dispute on land boundaries.
-----	---------------------------	---------	--------------------------	------	------------	-----	--------------------------	---------	--------	---



Kerala

22.	SAP Trivandrum B-Type+BW	2170.18	22.05.2014	CPWD	23.03.16	95%	15.06.17	2170.00	0.18	Slow progress due to shortage of funds. TDC-30.09.2018.
-----	-----------------------------	---------	------------	------	----------	-----	----------	---------	------	---



23.	Kanhagad ('A' Type+ 09 SQ+BW + covering)	2235.49	02.11.2015	CPWD	01.10.16	50%	28.12.17	1520.00	715.49	Delay due to dispute. TDC-30.09.18
-----	--	---------	------------	------	----------	-----	----------	---------	--------	------------------------------------



24.	Ezhimala ('A' Type + BW)	1991.24	24.04.2015	MES	17.08.2017	45%	17.07.19	420.00	1571.24	Delay on the part of MES.
-----	-----------------------------	---------	------------	-----	------------	-----	----------	--------	---------	---------------------------



25.	KPA, Ramavarmapuram ('B' Type+ 09 SQ+BW + covering)	2664.40	20.07.2016	CPWD	20.05.17	32%	13.08.18	820.00	1844.40	TDC-30.05.2019
-----	---	---------	------------	------	----------	-----	----------	--------	---------	----------------



Madhya Pradesh

26.	Chaurai A-Type+9SQ+BW	1284.56	17.06.15	CPWD	25.03.16	36%	24.03.17	620.00	664.56	Slow Progress/Shortage of funds. TDC-30.09.2018
-----	--------------------------	---------	----------	------	----------	-----	----------	--------	--------	--



27.	No2 Chindwada ('A' Type+ 09 SQ+BW + covering)	1462.89	21.07.2016	CPWD	01.01.17	23%	31.12.17	620.00	842.89	Work is being started shortly.TDC-31.03.2019.
-----	---	---------	------------	------	----------	-----	----------	--------	--------	--



28.	No-2 Satna ('A'- Type+SQ+BW)	1926.35	07.12.2015 20.12.2016	UPJN	03.01.17	78%	02.01.2019	1920.00	6.35	Work in progress.
-----	----------------------------------	---------	--------------------------	------	----------	-----	------------	---------	------	-------------------



29.	Betul ('A' Type+ 09 SQ+BW + covering)	1647.29	20.07.2016	CPWD	02.12.16	65%	01.02.18	1020.00	627.29	Slow progress/Shortage of funds.
-----	---------------------------------------	---------	------------	------	----------	-----	----------	---------	--------	----------------------------------



30.	Dindori ('A' Type+ 09 SQ+BW + covering)	1604.72	21.07.2016	CPWD	01.01.2017	80%	31.12.2017	1520.00	84.72	Work Started. TDC-30.6.18
-----	---	---------	------------	------	------------	-----	------------	---------	-------	---------------------------



Maharashtra										
31.	Nanded ('A'type+ 09 SQ+ BW)	2276.52	19.05.2016 08.09.2016	UPJN	15.09.16	82%	14.09.18	2120.00	156.52	Work in Progress.



32.	BSF, Chakur('A' Type+ 09 SQ + BW)	1794.90	01.03.17	UPJN	21.03.2017	39%	20.03.2019	1220.00	574.90	Work in Progress
-----	-----------------------------------	---------	----------	------	------------	-----	------------	---------	--------	------------------



Mizoram										
33.	Champai ('A-' Type+ 09 SQ + BW)	2723.98	18.02.2015	CPWD	10.07.16	48%	01.03.18	2420.00	303.98	N.E. Region Problem.



Odisha										
34.	Nayagarh ('A' - Type, SB +09 SQ+ BW + Covering of Courtyard)	1639.01	28.07.16	CPWD	13.12.16	75%	12.12.17	1220.00	419.01	Work In Progress. TDC-31.12.18



35.	No.2 Sambalpur ('A' Type+09 SQ+BW)	1646.17	20-06-2016 28.02.2017	BBJ&JCC	14.04.17	52%	Aug,2018	920.00	726.17	Work in Progress.
-----	------------------------------------	---------	--------------------------	---------	----------	-----	----------	--------	--------	-------------------



36.	Aska ('A' Type SB+09+ SQ+BW)	1701.86	16.05.17	CPWD	21.08.17	20%	20.01.19	820.00	881.86	Work in Progress.
-----	------------------------------	---------	----------	------	----------	-----	----------	--------	--------	-------------------



37.	Mahuldiha ('A Type+ 09 SQ)	1605.28	07.04.17	CPWD	25.08.17	80%	24.08.18	1020.00	585.28	Work in Progress. TDC-30.11.18
-----	----------------------------	---------	----------	------	----------	-----	----------	---------	--------	-----------------------------------



Puducherry

38.	Mahe ('A-1' Type + BW)	1837.52	02.11.2015	CPWD	27.07.17	30%	21.07.2018	820.00	1017.52	Matter is being resolved by Principal. Work suspended due to intervention of local public.TDC-26.09.2018
-----	------------------------	---------	------------	------	----------	-----	------------	--------	---------	---



Rajasthan

39.	Hanumangarh ('A' Type + 09 SQ + BW)	1605.31	06.10.15 28.06.16	HSCL	23.11.16	84%	23.05.18	1320.00	285.31	Work in progress.
-----	-------------------------------------	---------	----------------------	------	----------	-----	----------	---------	--------	-------------------



40.	Jalore ('B' Type + 09 SQ + BW)	2028.68	19.07.2016	UPSCIDCO	27.09.16	60%	31.03.18	1520.00	508.68	Work in progress. TDC- 31.12.18
-----	--------------------------------	---------	------------	----------	----------	-----	----------	---------	--------	---------------------------------



Telangana

41.	Miryalguda A-Type+09SQ+BW	1525.95	23.02.2016	HSCL	March 2016	67%	09.03.17	1420.00	105.03	Work in progress. Initial delay due to land problem. TDC- 31.12.2018
-----	---------------------------	---------	------------	------	------------	-----	----------	---------	--------	--



Tamil Nadu

42.	Perambalur ('A' Type + 09 SQ + BW+ Courtyard covering)	1874.02	20.07.16	CPWD	Work Awarded on 03.01.17	75%	23.04.18	1420.00	454.02	Work in Progress. TDC – 30.08.2018
-----	---	---------	----------	------	--------------------------	-----	----------	---------	--------	------------------------------------



Uttar Pradesh

43.	No-4, Varanasi A-Type+09SQ BW	1369.52	24.11.2014	HSLC	25.05.15	12%	10.11.16	220.00	1149.52	Go ahead issued to restart the work on 07.05.2018, TDC-30.11.19
-----	-------------------------------------	---------	------------	------	----------	-----	----------	--------	---------	---



44.	Siddarthnagar (B Type SB + 09 SQ+BW)	1820.28	16.05.17	CPWD	14.02.18	20%	13.08.19	720.00	1100.28	Works recently sanctioned. Work held up due to HT Line in LOP.
-----	---	---------	----------	------	----------	-----	----------	--------	---------	--



45.	Sharawasti ('A' Type+09 SO+BW)	1585.12	20-06-2016 07.04.2017	BBJ&JCC	16.04.18	4%	Sep 2019	220.00	1365.12	Go-ahead issued to restart the work on 26.03.18
-----	-----------------------------------	---------	--------------------------	---------	----------	----	----------	--------	---------	---



West Bengal

46.	Balurghat A type + 11 SQ + BW	1978.34	26.06.2014	CPWD	23.01.16	95%	22.05.17	1970.00	8.34	Delay in handling over of land TDC-31.12.18
-----	-------------------------------------	---------	------------	------	----------	-----	----------	---------	------	--



47.	Kalimpong ('A-1' + BW)	1430.74	10.12.2014	MES	16.11.15	37%	Dec 2019	620.00	810.74	Slow Progress.
-----	----------------------------	---------	------------	-----	----------	-----	----------	--------	--------	-----------------------



Lakhasdweep

48.	Kavarati A-I type+11 SQ+BW	2325.64	02.02.2015	CPWD	12.02.16	79%	04.08.17	2120.00	205.64	Initial slow progress. Now progressing well. TDC-30.06.18
-----	-------------------------------	---------	------------	------	----------	-----	----------	---------	--------	--



WORK YET TO BE STARTED

Sl. No.	Name of Kendriya Vidyalyaya	AA & ES (Rs. in lakh)	Date of Sanction	Construction Agency	Date of Start	Physical Progress upto date	Stipulated date of completion	Amount released till 01.09.2016 (Rs. in lakh)	Balance liability (Rs. in lakh)	Remark
Assam										
1.	Barpeta (A-Type+9SB+B/w)	2525.19	03.10.2018	CPWD	20.00	2505.19	Work yet to start
Bihar										
2	Bela (A-Type +09SQ+BW)	2001.95	22.11.2016	CPWD	220.00	1781.95	Work recently sanctioned and at tender stage.
3.	Harnaut('A'Type+09SQ+BW)	2015.01	16.05.2017	CPWD	20.00	1995.01	Tender recently accepted.
4.	Jhajha ('A' Type+09SQ+BW)	1975.82	03.10.2018	CPWD	20.00	1955.82	Work yet to start.
Daman & Diu										
5.	Diu ('A' Type + 09 SQ+BW)	2089.49	27.08.2018	CPWD	Work yet to start	20.00	2069.49	
Dadar & Nagar Haveli										
6.	Silvassa ('A' Type + 09 SQ+BW)	1558.04	14.08.2018	CPWD	Work yet to start	20.00	1538.04	
Delhi										
7.	3Sec.-22, Rohini ('B' Type)	746.11	03.10.2007	CPWD	Work yet to start	0.00	746.11	Drawing yet to be approved by local bodies. Permission for demolishing of temporary structure awaited
8.	Shahdara ('A' Type S/B)	1460.12	13.04.2018	CPWD	500.00	960.12	Work recently sanctioned
Gujarat										
	AFS Jamnagar (Replacement of SB)	1559.14	02.05.2018	MES	...	Work yet to start	...	20.00	1539.14	
Haryana										
9.	Mathana ('A' Type SB+ 9SQ+BW)	1801.5	07.08.2018	CPWD	...	Work yet to start	20.00	1781.50	

Himachal Pradesh										
10.	Saloh (‘A’ Type + 09 SQ)	1620.95	21.06.2017	BSNL		5.00	1615.95	IIT vetting is awaited from BSNL to issue go-ahead.
11.	Nadaun(‘A-1’Type+09 SQ+BW)	1314.4	01.08.2018	CPWD	20.00	1294.40	Work Just Sanctioned.
12.	Reckong Peo (‘A’ Type + 09 SQ+BW)	2585.03	03.10.2018	CPWD	20.00	2565.03	Work just Sanctioned.
Karnataka										
13.	Haveri (‘A’ Type + 09 SQ + BW)	2061.80	01.09.2016	FEDO	0.00	2061.80	Work Yet to start.
Kerala										
14.	Kaduruthy (‘A’ Type B+09 SQ +BW+covering)	3020.62	27.12.2016	FEDO	0%	0.00	3020.62	Work yet to start.
Madhya Pradesh										
15.	Harda (A-Type+9SQ+BW)	1651.25	19.09.2016	FEDO	0%	0.00	1651.25	Work Yet to Start.
16.	Malanj Khan (‘A’ Type SB +9 SQ+BW)	1831.62	28.06.2017	UPJN	...	0%	...	0.00	1811.62	Work Yet to Start.
17.	Pandurana (‘A-Type + 09 SQ+ BW)	1783.61	01.08.2018	CPWD	...	0%	...	20.00	1859.16	Work Just Sanctioned.
Maharashtra										
	AFS Thane (Replacement of SB)	1204.89	02.05.2018	MES	...	Work yet to start	...	20.00	1184.89	
Mizoram										
18.	Lunglai (‘A’ Type+ 09 SQ + BW)	2385.37	24.11.2014 02.05.2017	MAMCO	20.00	2365.37	Work Yet to Start

Odisha										
19.	Sonepur ('A' Type SB+ 09 SQ+BW)	1580.85	01.08.2018	CPWD	20.00	1360.85	Work Just Sanctioned.
20.	Kutra ('A-1' Type SB+09+SQ+BW)	1310.12	03.10.2018	CPWD	20.00	1290.12	Work Just Sanctioned.
21.	Mundali ('A' Type SB+09+BW)	2094.25	31.10.2018	CPWD	20.00	2074.25	Work Just Sanctioned.
Rajasthan										
22.	Devgarh ('A' Type SB+ 09 SQ)	1436.72	16.05.2017	CPWD	20.00	1695.41	Work Yet to Start
23.	Tonk ('A-1' Type SB + 09 SQ)	1011.80	21.06.2017	CPWD	20.00	991.80	Work Yet to Start
Tamilnadu										
24.	AFS, Tanjavur 'A' Type + 09 SQ + BW)	1835.59	02.11.2015	MES	220.00	1615.59	Delay on the part of MES.
Telangana										
25.	Sirsilla ('A' Type SB+ 09 SQ+ BW)	1651.61	16.03.2017	HSCL		1651.61	Work Yet to Start
Uttar Pradesh										
26.	Deoria ('A' Type + 09 SQ + BW)	1415.74	25.06.2013	CPWD	...	Work yet to start	...	70.00	1345.74	Encroachment on land.
27.	Gangarani, Kushinagar (B Type SB + 09 SQ+BW)	1680.66	26.04.17	CPWD	500.00	1180.66	Tender recently accepted
Uttarakhand										
28.	Bhimtal (A Type +BW+Covering)	1792.79	21.03.2017	CPWD	20.00	1772.79	Work Yet to Start
29.	Gopeshwar ('A-1 Type SB+09+ SQ+B/W)	2185.97	26.06.2017	UPJN		2185.97	Work Yet to Start
